Sprint planning meeting

Sprint planning meeting

Who

Vương Phi Long - ITITIU21238

Nguyễn Hồng Sơn - ITITIU20294

Bùi Văn Tiến Đạt - ITITWE20005

……..

……..

……..

Agenda (*list your activities in the meeting*)

1. Review sprint goal and acceptance criteria

2. Present and estimate user stories for the sprint backlog

3. Break stories into tasks and assign owners

4. Agree on definition of done and testing strategy

5. Identify risks and dependencies

6. Confirm sprint schedule and demo date

Why (*explain your decisions on the product backlog and the first print backlog*)

This sprint focuses on delivering the minimum viable features for the Employee Attendance System so the team can run an end-to-end demo: employee CRUD, clock in/out, shift assignment, and a basic leave request flow. Delivering these features enables early feedback from stakeholders and validates the core data model and APIs.

Product Backlog

Backlog item (user story)	Estimate (days)	Priority
ST-01: Admin can create/read/update/delete employee profiles to maintain accurate records.	**3**	**High**

ST-02: Employees can clock in and clock out from a web/mobile interface to record work time.	**4**	**High**
ST-06: Infrastructure: Set up database migrations, seed data, and CI pipeline for tests.	**3**	**High**
ST-04: Employee leave request submission and manager approval/rejection workflow.	**4**	**Mediu m**
ST-03: Managers can assign shifts to employees for specific date ranges to clear schedules.	**4**	**Mediu m**
ST-05: Managers can view team attendance summary reports (total hours, absences).	**3**	**Mediu m**
ST-07: Implement User Roles and Permissions to ensure secure access and data privacy.	**2**	**High**
ST-08: Compliance Tracking to monitor adherence to organizational attendance policies.	**5**	**Low**

Sprint goal: (*choose one backlog item to be carried out first*)

Implement core attendance features to support daily use by employees and managers: employee management (CRUD), reliable time clock in/out endpoints, shift assignment UI, and leave request + approval workflow. Ensure basic reporting for total work hours.

Sprint backlog (*for the chosen backlog item*)

Task / Day	Mon	Tue	Wed	Thu	Fri	Sat	Sun

T1: DB schema & migrations (ST-01, ST-06)	**Design schema**	**Create migrations**	**Review**	**Fix comments**	**Seed data**		
T2: Employee CRUD API (ST-01)	**API endpoints**	**Unit tests**	**Integrate with DB**	**API review**	**Bug fixes**		
T3: Timeclock endpoints (ST-02)	**Design contract**	**Implement clock-in**	**Implement clock-out**	**Business logic (work minutes)**	**Integration tests**		
T4: Shift assignment UI (ST-03)	**Design UI**	**Implement components**	**Connect API**	**E2E test**	**Polish UX**		
T5: Leave request flow (ST-04)	**Create form**	**API endpoint**	**Manager approval UI**	**Notification hooks**	**Test cases**		
T6: Reporting & Demo prep (ST-05)	**Basic report API**	**Frontend summary view**	**QA checks**	**Prepare demo script**	**Dry run**		
T7: CI/CD & Deployment (ST-06)	**Setup GitHub Actions**	**Docker Compose**	**Staging deploy**	**Backup script**	**Run tests**		

A Sprint Burndown Chart

This table is an initial burndown projection for the sprint. Update daily with actual remaining story points.

Day	**Mon**	**Tue**	**Wed**	**Thu**	**Fri**	**Sat**	**Sun**

Remaining Story Points	**40**	**34**	**28**	**20**	**12**	**6**	**0**

PROJECT PLAN DOCUMENT

PROJECT PLAN DOCUMENT

EMPLOYEE ATTENDANCE SYSTEM

I. Overview:

The Employee Attendance System is designed to help organizations manage employee attendance records efficiently. The system allows administrators to track employee check-in/check-out times, manage leave requests, generate attendance reports, and monitor employee performance.

II. Goals and scope:

a) Goals:

- Automate attendance tracking
- Reduce manual paperwork
- Improve HR efficiency
- Generate attendance reports

b) Scope:

In scope:

- Employee registration
- Check-in / check-out
- Leave request
- Attendance report
- Admin dashboard

Out of scope:

- Payroll calculation
- Biometric integration
- Mobile app version

III. Organization:

Member's name	Team role	Phone number	Email address
Vương Phi Long	Designer	0961189637	ITITIU21238@student.edu.hcmiu.vn
Nguyễn Hồng Sơn	Designer	0765534408	ITITIU20294@student.edu.hcmiu.vn
Bui Van Tien Dat	Programmer		

IV. Resource requirements:

1/ Hardware resources:

Items	Quantity	Description	Purpose	Price	Total Cost	Date needed
Lenovo System x3500 M5	**1**	**System Server**	**Data Server**	**….**	**….**	**27/2/2026**
Router	**1**	**Network device**	**Network connection**	**…**	**…**	**27/2/2026**
Total Cost:						

2/ Software resources:

Application	Quantity	Description	Purpose	Price	Total Cost	Date needed
MS Windows 11 64bit	3	Operating System	PC's OS	free	$0	27/2/2026
MySQL	1	Database management system	Store employee data	free	$0	27/2/2026
Visual studio code	3	Code editor	Programming	free	$0	27/2/2026
Total Cost:						

3/ Human resources:

Name	Name of Organization	Project Role	Required Skills	Phone	Email	Salary/month
….	**….**	**Project Manager**	**…….**	**……**	**…..**	**……**

…..	….	Business Analyst	…..	…..	…..	…..
Total Cost:						

V. Schedule:

1/ Work breakdown structure:

Following the Software Development Life Cycle, the process includes: Requirement Analysis, Design, Implementation, Testing, Deployment and Maintenance.



Then, in each phase, you break it into smaller tasks. For example, in the Analysis phase, you can break into 3 activities, which are Gathering business requirements, creating process diagrams, and performing a detailed analysis.

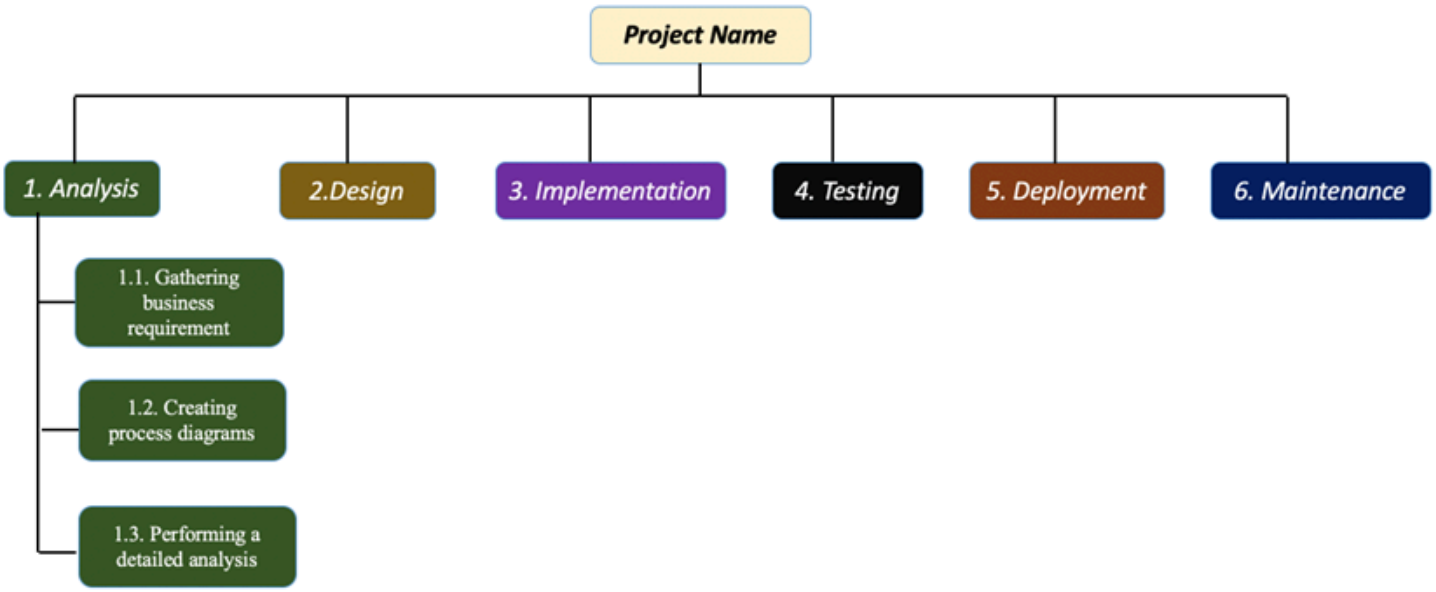

Then, continue breaking them into smaller ones.

2/ Schedule and milestones:

VI. Risk management:

Risk ID	Risk Category	Risk Title	Affect	Probability	Impact	Risk response plan
001	HR	Members lack of team corporation, or weak participation	This can slow down the progress of the project, produce unreliable result from the uncooperative work	Medium	Low	Organize team members so that they can easily get along with each other. Solve all the conflicts that are existing among the team members
002	Requirements	Additional requirements are added	It effects on the project progress	High	Medium	Hold a meeting to update schedule and plan
003	Organization and Management	Project is running over the budget	The project has to be stopped if the team ran out of the budget	Medium	High	Project Manager must propose a new saving plan or financial management

VII. Delivery plan

VIII. Security aspects:

IX. Abbreviations and Definitions

X. References:

XI. Product backlog:

Backlog item (user story)	Estimate (days)	Priority

ST-01: Admin can create/read/update/delete employee profiles to maintain accurate records.	**3**	**High**
ST-02: Employees can clock in and clock out from a web/mobile interface to record work time.	**4**	**High**
ST-06: Infrastructure: Set up database migrations, seed data, and CI pipeline for tests.	**3**	**High**
ST-04: Employee leave request submission and manager approval/rejection workflow.	**4**	**Mediu m**
ST-03: Managers can assign shifts to employees for specific date ranges to clear schedules.	**4**	**Mediu m**
ST-05: Managers can view team attendance summary reports (total hours, absences).	**3**	**Mediu m**
ST-07: Implement User Roles and Permissions to ensure secure access and data privacy.	**2**	**High**
ST-08: Compliance Tracking to monitor adherence to organizational attendance policies.	**5**	**Low**

XII. Sprint backlogs:

Task / Day	Mon	Tue	Wed	Thu	Fri	Sat	Sun
T1: DB schema & migrations	Design schema	Create migrations	Review	Fix comments	Seed data		

(ST-01, ST-06)							
T2: Employee CRUD API (ST-01)	API endpoints	Unit tests	Integrate with DB	API review	Bug fixes		
T3: Timeclock endpoints (ST-02)	Design contract	Implement clock-in	Implement clock-out	Business logic (work minutes)	Integration tests		
T4: Shift assignment UI (ST-03)	Design UI	Implement components	Connect API	E2E test	Polish UX		
T5: Leave request flow (ST-04)	Create form	API endpoint	Manager approval UI	Notification hooks	Test cases		
T6: Reporting & Demo prep (ST-05)	Basic report API	Frontend summary view	QA checks	Prepare demo script	Dry run		
T7: CI/CD & Deployment (ST-06)	Setup GitHub Actions	Docker Compose	Staging deploy	Backup script	Run tests		

A Sprint Burndown Chart

This table is an initial burndown projection for the sprint. Update daily with actual remaining story points.

Day	Mon	Tue	Wed	Thu	Fri	Sat	Sun
Remaining Story Points	40	34	28	20	12	6	0

XIII. Members’ contributions:
